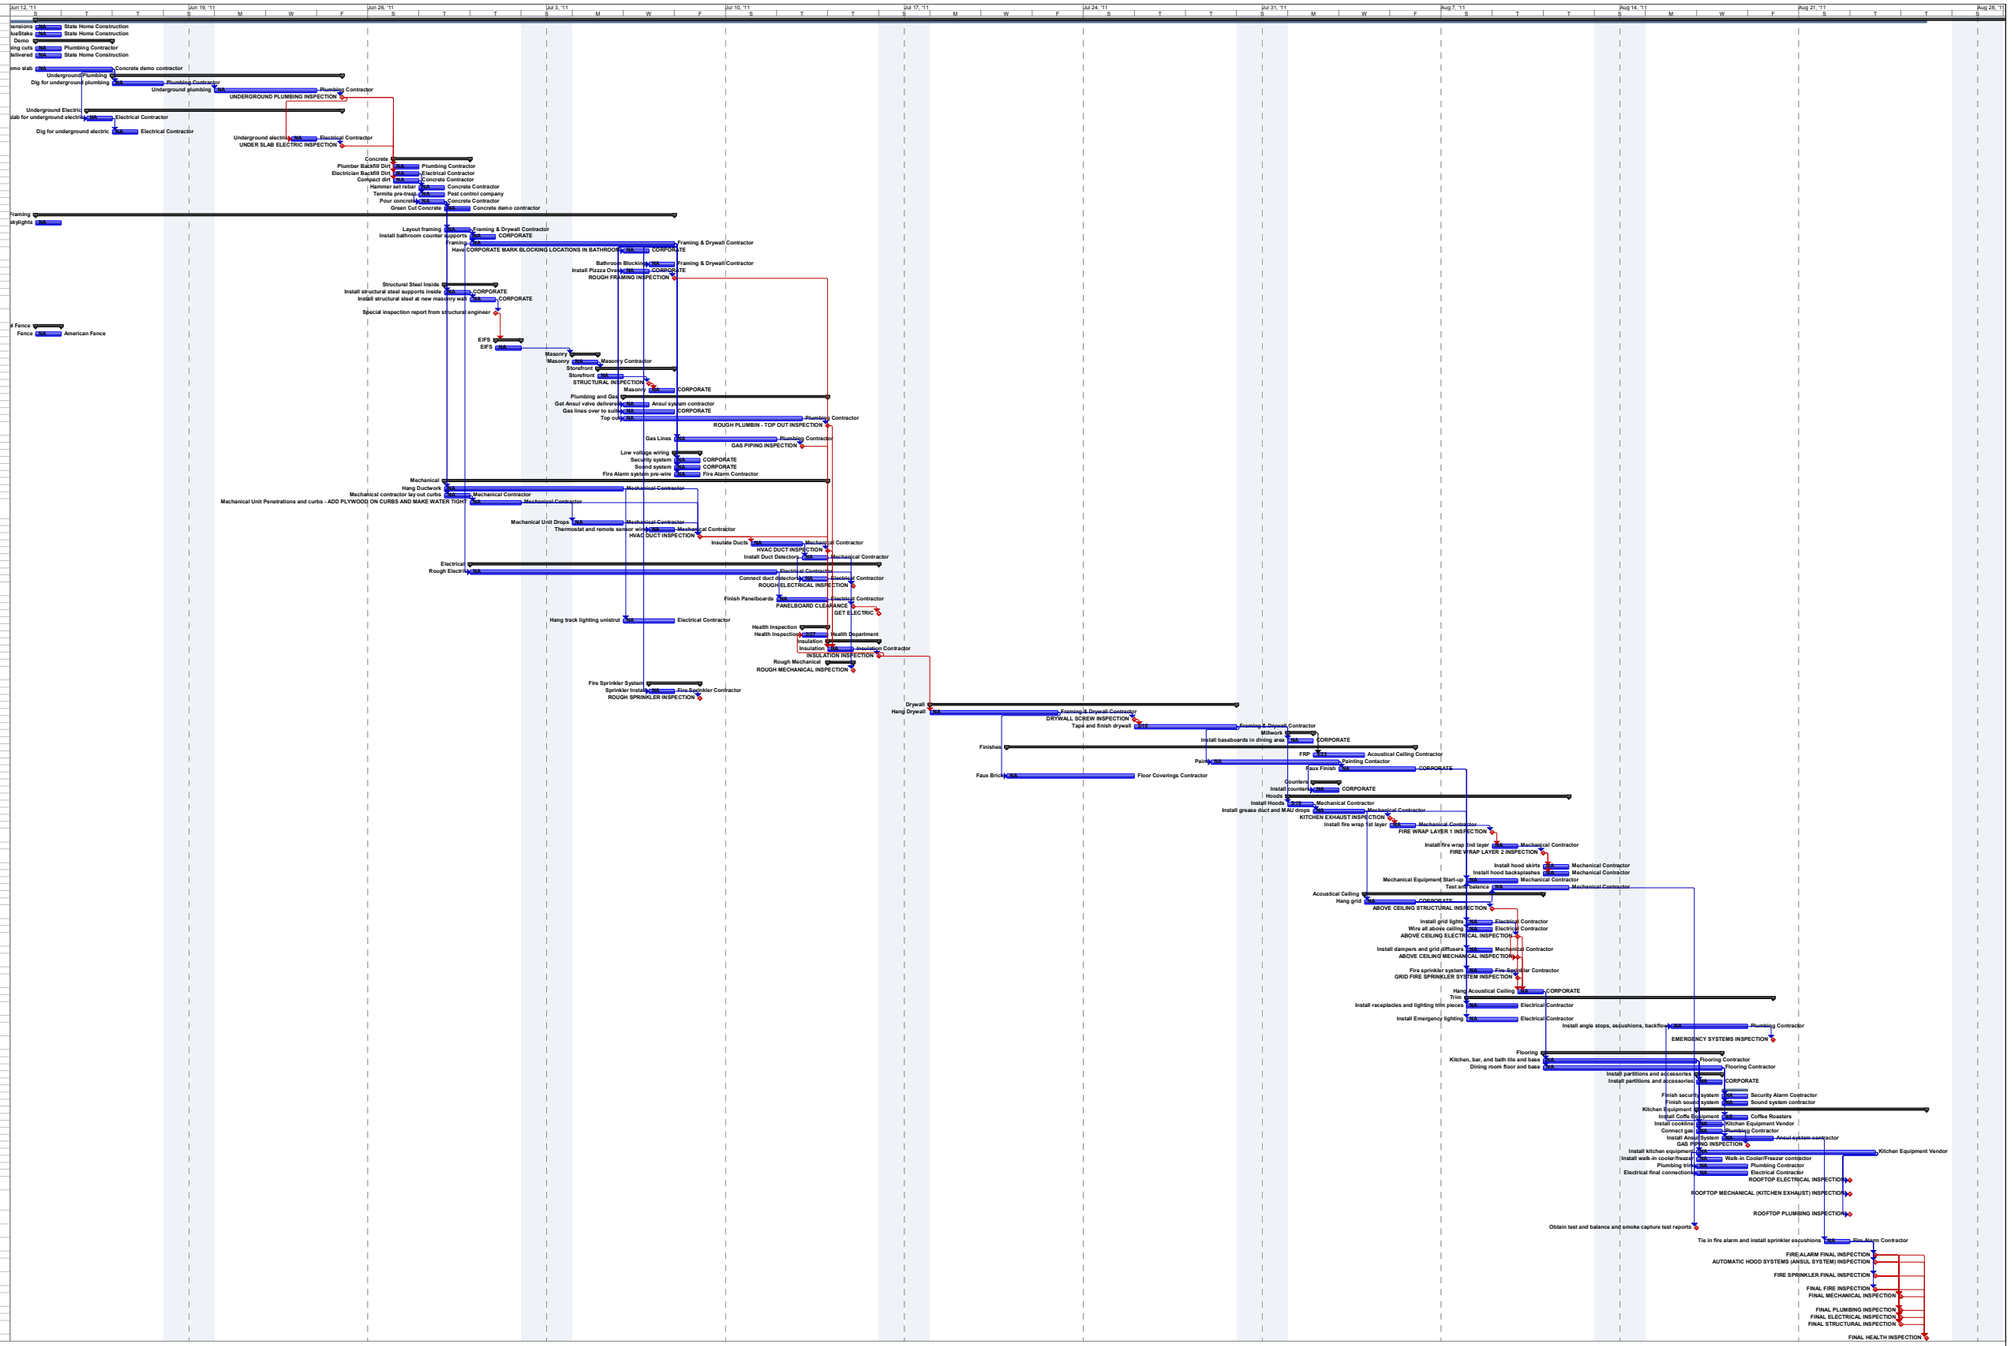ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**PITA JUNGLE ROOSEVELT PROJECT**	**60 days?**	**Mon 6/13/11**	**Fri 9/2/11**		
2	Verify building dimensions	1 day	Mon 6/13/11	Mon 6/13/11		State Home Construction
3	Call BlueStake	1 day	Mon 6/13/11	Mon 6/13/11		State Home Construction
4	**Demo**	**3 days**	**Mon 6/13/11**	**Wed 6/15/11**		
5	Layout for plumbing cuts	1 day	Mon 6/13/11	Mon 6/13/11		Plumbing Contractor
6	Have Dumpster and port-o-john delivered	1 day	Mon 6/13/11	Mon 6/13/11		State Home Construction
7	Saw cut and demo slab	3 days	Mon 6/13/11	Wed 6/15/11		Concrete demo contractor
8	**Underground Plumbing**	**7 days**	**Thu 6/16/11**	**Fri 6/24/11**		
9	Dig for underground plumbing	2 days	Thu 6/16/11	Fri 6/17/11	7	Plumbing Contractor
10	Underground plumbing	4 days	Mon 6/20/11	Thu 6/23/11	9	Plumbing Contractor
11	*UNDERGROUND PLUMBING INSPECTION*	*1 day*	*Fri 6/24/11*	*Fri 6/24/11*	*10*	Phoenix Building Inspector
12	**Underground Electric**	**8 days**	**Wed 6/15/11**	**Fri 6/24/11**		
13	Saw cut slab for underground electric	1 day	Wed 6/15/11	Wed 6/15/11	7FS-1 day	Electrical Contractor
14	Dig for underground electric	1 day	Thu 6/16/11	Thu 6/16/11	13	Electrical Contractor
15	Underground electric	1 day	Thu 6/23/11	Thu 6/23/11	11FS-2 days	Electrical Contractor
16	*UNDER SLAB ELECTRIC INSPECTION*	*1 day*	*Fri 6/24/11*	*Fri 6/24/11*	*15*	Phoenix Building Inspector
17	**Concrete**	**3 days**	**Mon 6/27/11**	**Wed 6/29/11**		
18	Plumber Backfill Dirt	1 day	Mon 6/27/11	Mon 6/27/11	11	Plumbing Contractor
19	Electrician Backfill Dirt	1 day	Mon 6/27/11	Mon 6/27/11	16	Electrical Contractor
20	Compact dirt	1 day	Mon 6/27/11	Mon 6/27/11	11	Concrete Contractor
21	Hammer set rebar	1 day	Tue 6/28/11	Tue 6/28/11	18	Concrete Contractor
22	Termite pre-treat	1 day	Tue 6/28/11	Tue 6/28/11	20	Pest control company
23	Pour concrete	1 day	Tue 6/28/11	Tue 6/28/11	22FS-1 day	Concrete Contractor
24	Green Cut Concrete	1 day	Wed 6/29/11	Wed 6/29/11	23	Concrete demo contractor
25	**Framing**	**19 days**	**Mon 6/13/11**	**Thu 7/7/11**		
26	Make Penetrations for skylights	1 day	Mon 6/13/11	Mon 6/13/11		
27	Layout framing	1 day	Wed 6/29/11	Wed 6/29/11	23	Framing & Drywall Contractor
28	Install bathroom counter supports	1 day	Thu 6/30/11	Thu 6/30/11	27	CORPORATE
29	Framing	6 days	Thu 6/30/11	Thu 7/7/11	27	Framing & Drywall Contractor
30	Have CORPORATE MARK BLOCKING LOCATIONS IN BATHROOM	1 day	Wed 7/6/11	Wed 7/6/11	29FS-2 days	CORPORATE
31	Bathroom Blocking	1 day	Thu 7/7/11	Thu 7/7/11	29FS-1 day	Framing & Drywall Contractor
32	Install Pizza Oven	1 day	Wed 7/6/11	Wed 7/6/11	29FS-2 days	CORPORATE
33	*ROUGH FRAMING INSPECTION*	*1 day*	*Thu 7/7/11*	*Thu 7/7/11*	*32*	Phoenix Building Inspector
34	**Structural Steel Inside**	**2 days**	**Wed 6/29/11**	**Thu 6/30/11**		
35	Install structural steel supports inside	1 day	Wed 6/29/11	Wed 6/29/11	23	CORPORATE
36	Install structural steel at new masonry wall	1 day	Thu 6/30/11	Thu 6/30/11	35	CORPORATE
37	Special inspection report from structural engineer	0 days	Thu 6/30/11	Thu 6/30/11	36	CORPORATE
38	**Install Rental Fence**	**1 day?**	**Mon 6/13/11**	**Mon 6/13/11**		
39	Fence	1 day?	Mon 6/13/11	Mon 6/13/11		American Fence
40	**EIFS**	**1 day?**	**Fri 7/1/11**	**Fri 7/1/11**	37	
41	EIFS	1 day?	Fri 7/1/11	Fri 7/1/11		
42	**Masonry**	**1 day?**	**Mon 7/4/11**	**Mon 7/4/11**	41	
43	Masonry	1 day?	Mon 7/4/11	Mon 7/4/11		Masonry Contractor
44	**Storefront**	**3 days?**	**Tue 7/5/11**	**Thu 7/7/11**	43	
45	Storefront	1 day?	Tue 7/5/11	Tue 7/5/11		
46	*STRUCTURAL INSPECTION*	*1 day*	*Thu 7/7/11*	*Thu 7/7/11*	*45*	Phoenix Building Inspector
47	Masonry	1 day?	Thu 7/7/11	Thu 7/7/11	46	CORPORATE
48	**Plumbing and Gas**	**6 days**	**Wed 7/6/11**	**Wed 7/13/11**		
49	Get Ansul valve delivered	1 day	Wed 7/6/11	Wed 7/6/11	29FS-2 days	Ansul system contractor
50	Gas lines over to suite	2 days	Wed 7/6/11	Thu 7/7/11	29FS-2 days	CORPORATE
51	Top out	5 days	Wed 7/6/11	Tue 7/12/11	29FS-2 days	Plumbing Contractor
52	*ROUGH PLUMBIN - TOP OUT INSPECTION*	1 day	Wed 7/13/11	Wed 7/13/11	51	Phoenix Building Inspector
53	Gas Lines	2 days	Fri 7/8/11	Mon 7/11/11	29	Plumbing Contractor
54	*GAS PIPING INSPECTION*	1 day	Tue 7/12/11	Tue 7/12/11	53	Phoenix Building Inspector
55	**Low voltage wiring**	**1 day**	**Fri 7/8/11**	**Fri 7/8/11**		
56	Security system	1 day	Fri 7/8/11	Fri 7/8/11	29	CORPORATE
57	Sound system	1 day	Fri 7/8/11	Fri 7/8/11	29	CORPORATE
58	Fire Alarm system pre-wire	1 day	Fri 7/8/11	Fri 7/8/11	29	Fire Alarm Contractor
59	**Mechanical**	**11 days**	**Wed 6/29/11**	**Wed 7/13/11**		**Mechanical Contractor**
60	Hang Ductwork	5 days	Wed 6/29/11	Tue 7/5/11	23	Mechanical Contractor
61	Mechanical contractor lay out curbs	1 day	Wed 6/29/11	Wed 6/29/11	23	Mechanical Contractor
62	Mechanical Unit Penetrations and curbs - ADD PLYWOOD ON CURBS AND MAKE WATER TIGHT	2 days	Thu 6/30/11	Fri 7/1/11	61	Mechanical Contractor
63	Mechanical Unit Drops	2 days	Mon 7/4/11	Tue 7/5/11	62	Mechanical Contractor
64	Thermostat and remote sensor wire	1 day	Thu 7/7/11	Thu 7/7/11	29FS-1 day	Mechanical Contractor
65	*HVAC DUCT INSPECTION*	1 day	Fri 7/8/11	Fri 7/8/11	63,60,62,64	Mechanical Contractor
66	Insulate Ducts	2 days	Mon 7/11/11	Tue 7/12/11	65	Mechanical Contractor
67	*HVAC DUCT INSPECTION*	1 day	Wed 7/13/11	Wed 7/13/11	66	Phoenix Building Inspector
68	Install Duct Detectors	1 day	Wed 7/13/11	Wed 7/13/11	66	Mechanical Contractor
69	**Electrical**	**12 days**	**Thu 6/30/11**	**Fri 7/15/11**		
70	Rough Electric	8 days	Thu 6/30/11	Mon 7/11/11	29	Electrical Contractor
71	Connect duct detectors	1 day	Wed 7/13/11	Wed 7/13/11	68	Electrical Contractor
72	*ROUGH ELECTRICAL INSPECTION*	1 day	Thu 7/14/11	Thu 7/14/11	70,71	Phoenix Building Inspector
73	Finish Panelboards	2 days	Tue 7/12/11	Wed 7/13/11	70	Electrical Contractor
74	*PANELBOARD CLEARANCE*	1 day	Thu 7/14/11	Thu 7/14/11	73	Phoenix Building Inspector
75	*GET ELECTRIC*	1 day	Fri 7/15/11	Fri 7/15/11	74	Electric Company CORPORATE
76	Hang track lighting unistrut	2 days	Wed 7/6/11	Thu 7/7/11	60	Electrical Contractor
77	**Health Inspection**	**1 day**	**Wed 7/13/11**	**Wed 7/13/11**		
78	Health Inspection	1 day	Wed 7/13/11	Wed 7/13/11	8 FS-3 days	Health Department
79	**Insulation**	**2 days**	**Thu 7/14/11**	**Fri 7/15/11**		
80	Insulation	1 day	Thu 7/14/11	Thu 7/14/11	33,52,54,65,67	Insulation Contractor
81	*INSULATION INSPECTION*	1 day	Fri 7/15/11	Fri 7/15/11	80	Phoenix Building Inspector
82	**Rough Mechanical**	**1 day**	**Thu 7/14/11**	**Thu 7/14/11**		
83	*ROUGH MECHANICAL INSPECTION*	1 day	Thu 7/14/11	Thu 7/14/11	68	Phoenix Building Inspector
84	**Fire Sprinkler System**	**2 days**	**Thu 7/7/11**	**Fri 7/8/11**		
85	Sprinkler Install	1 day	Thu 7/7/11	Thu 7/7/11	29FS-1 day	Fire Sprinkler Contractor
86	*ROUGH SPRINKLER INSPECTION*	1 day	Fri 7/8/11	Fri 7/8/11	85	Fire Marshall
87	**Drywall**	**10 days**	**Mon 7/18/11**	**Fri 7/29/11**		
88	Hang Drywall	5 days	Mon 7/18/11	Fri 7/22/11	81	Framing & Drywall Contractor
89	*DRYWALL SCREW INSPECTION*	1 day	Mon 7/25/11	Mon 7/25/11	88	Phoenix Building Inspector
90	Tape and finish drywall	4 days	Tue 7/26/11	Fri 7/29/11	89	Framing & Drywall Contractor
91	**Millwork**	**1 day**	**Mon 8/1/11**	**Mon 8/1/11**		
92	Install baseboards in dining area	1 day	Mon 8/1/11	Mon 8/1/11	90	CORPORATE
93	**Finishes**	**12 days**	**Thu 7/21/11**	**Fri 8/5/11**		
94	FRP	2 days	Tue 8/2/11	Wed 8/3/11	91	Acoustical Ceiling Contractor
95	Paint	3 days	Fri 7/29/11	Tue 8/2/11	90FS-1 day	Painting Contactor
96	Faux Finish	3 days	Wed 8/3/11	Fri 8/5/11	95	CORPORATE
97	Faux Brick	3 days	Thu 7/21/11	Mon 7/25/11	88FS-2 days	Floor Coverings Contractor
98	**Counters**	**1 day**	**Tue 8/2/11**	**Tue 8/2/11**		
99	Install counters	1 day	Tue 8/2/11	Tue 8/2/11	95FS-1 day	CORPORATE
100	**Hoods**	**9 days**	**Mon 8/1/11**	**Thu 8/11/11**		
101	Install Hoods	1 day	Mon 8/1/11	Mon 8/1/11	90	Mechanical Contractor
102	Install grease duct and MAU drops	2 days	Tue 8/2/11	Wed 8/3/11	101	Mechanical Contractor
103	*KITCHEN EXHAUST INSPECTION*	1 day	Thu 8/4/11	Thu 8/4/11	102	Phoenix Building Inspector
104	Install fire wrap 1st layer	1 day	Fri 8/5/11	Fri 8/5/11	103	Mechanical Contractor
105	*FIRE WRAP LAYER 1 INSPECTION*	1 day	Mon 8/8/11	Mon 8/8/11	104	Phoenix Building Inspector
106	Install fire wrap 2nd layer	1 day	Tue 8/9/11	Tue 8/9/11	105	Mechanical Contractor
107	*FIRE WRAP LAYER 2 INSPECTION*	1 day	Wed 8/10/11	Wed 8/10/11	106	Phoenix Building Inspector
108	Install hood skirts	1 day	Thu 8/11/11	Thu 8/11/11	107	Mechanical Contractor
109	Install hood backsplashes	1 day	Thu 8/11/11	Thu 8/11/11	107	Mechanical Contractor
110	Mechanical Equipment Start-up	2 days	Mon 8/8/11	Tue 8/9/11	102,113	Mechanical Contractor
111	Test and balance	3 days	Tue 8/9/11	Thu 8/11/11	113FS+1 day	Mechanical Contractor
112	**Acoustical Ceiling**	**5 days**	**Thu 8/4/11**	**Wed 8/10/11**		
113	Hang grid	2 days	Thu 8/4/11	Fri 8/5/11	102	CORPORATE
114	*ABOVE CEILING STRUCTURAL INSPECTION*	1 day	Mon 8/8/11	Mon 8/8/11	113	Phoenix Building Inspector
115	Install grid lights	1 day	Mon 8/8/11	Mon 8/8/11	113	Electrical Contractor
116	Wire all above ceiling	1 day	Mon 8/8/11	Mon 8/8/11	113	Electrical Contractor
117	*ABOVE CEILING ELECTRICAL INSPECTION*	1 day	Tue 8/9/11	Tue 8/9/11	115	Phoenix Building Inspector
118	Install dampers and grid diffusers	1 day	Mon 8/8/11	Mon 8/8/11	113	Mechanical Contractor
119	*ABOVE CEILING MECHANICAL INSPECTION*	1 day	Tue 8/9/11	Tue 8/9/11	117FS	Phoenix Building Inspector
120	Fire sprinkler system	1 day	Mon 8/8/11	Mon 8/8/11	113	Fire Sprinkler Contractor
121	*GRID FIRE SPRINKLER SYSTEM INSPECTION*	1 day	Tue 8/9/11	Tue 8/9/11	120	Phoenix Building Inspector
122	Hang Acoustical Ceiling	1 day	Wed 8/10/11	Wed 8/10/11	114,117,119,121	CORPORATE
123	**Trim**	**10 days**	**Mon 8/8/11**	**Fri 8/19/11**		
124	Install receptacles and lighting trim pieces	2 days	Mon 8/8/11	Tue 8/9/11	96	Electrical Contractor
125	Install Emergency lighting	2 days	Mon 8/8/11	Tue 8/9/11	96	Electrical Contractor
126	Install angle stops, escushions, backflow	3 days	Tue 8/16/11	Thu 8/18/11	138FS-2 days	Plumbing Contractor
127	*EMERGENCY SYSTEMS INSPECTION*	1 day	Fri 8/19/11	Fri 8/19/11	126	Phoenix Building Inspector
128	**Flooring**	**5 days**	**Thu 8/11/11**	**Wed 8/17/11**		
129	Kitchen, bar, and bath tile and base	4 days	Thu 8/11/11	Tue 8/16/11	122	Flooring Contractor
130	Dining room floor and base	5 days	Thu 8/11/11	Wed 8/17/11	122	Flooring Contractor
131	**Install partitions and accessories**	**1 day**	**Wed 8/17/11**	**Wed 8/17/11**		
132	Install partitions and accessories	1 day	Wed 8/17/11	Wed 8/17/11	129	CORPORATE
133	**Low Voltage**	**1 day**	**Fri 8/3/11**	**Fri 8/3/11**		
134	Finish security system	1 day	Thu 8/18/11	Thu 8/18/11	130	Security Alarm Contractor
135	Finish sound system	1 day	Thu 8/18/11	Thu 8/18/11	130	Sound system contractor
136	**Kitchen Equipment**	**7 days**	**Tue 8/16/11**	**Thu 8/25/11**		
137	Install Coffe Equipment	1 day	Thu 8/18/11	Thu 8/18/11	130	Coffee Roasters
138	Install cooklins	1 day	Wed 8/17/11	Wed 8/17/11	129	Kitchen Equipment Vendor
139	Connect gas	1 day	Wed 8/17/11	Wed 8/17/11	129	Plumbing Contractor
140	Install Ansul System	2 days	Thu 8/18/11	Fri 8/19/11	138	Ansul system contractor
141	*GAS PIPING INSPECTION*	1 day	Thu 8/18/11	Thu 8/18/11	139	Phoenix Building Inspector
142	Install kitchen equipment	5 days	Wed 8/17/11	Tue 8/23/11	129	Kitchen Equipment Vendor
143	Install walk-in cooler/freezer	1 day	Wed 8/17/11	Wed 8/17/11	129	Walk-in Cooler/Freezer contractor
144	Plumbing trim	2 days	Wed 8/17/11	Thu 8/18/11	142FS	Plumbing Contractor
145	Electrical final connections	2 days	Wed 8/17/11	Thu 8/18/11	142FS	Electrical Contractor
146	*ROOFTOP ELECTRICAL INSPECTION*	1 day	Mon 8/22/11	Mon 8/22/11	142FS-2 days	Phoenix Building Inspector
147	*ROOFTOP MECHANICAL (KITCHEN EXHAUST) INSPECTION*	1 day	Mon 8/22/11	Mon 8/22/11	142FS-2 days	Phoenix Building Inspector
148	*ROOFTOP PLUMBING INSPECTION*	1 day	Mon 8/22/11	Mon 8/22/11	142FS-2 days	Phoenix Building Inspector
149	Obtain test and balance and smoke capture test reports	0 days	Tue 8/16/11	Tue 8/16/11	111FS+3 days	Mechanical Contractor
150	Tie in fire alarm and install sprinkler escushions	1 day	Mon 8/22/11	Mon 8/22/11	140	Fire Alarm Contractor
151	*FIRE ALARM FINAL INSPECTION*	1 day	Tue 8/23/11	Tue 8/23/11	150	Fire Marshall
152	*AUTOMATIC HOOD SYSTEMS (ANSUL SYSTEM) INSPECTION*	1 day	Tue 8/23/11	Tue 8/23/11	150	Fire Marshall
153	*FIRE SPRINKLER FINAL INSPECTION*	1 day	Tue 8/23/11	Tue 8/23/11	150	Fire Marshall
154	*FINAL FIRE INSPECTION*	1 day	Tue 8/23/11	Tue 8/23/11	150	Fire Marshall
155	*FINAL MECHANICAL INSPECTION*	1 day	Wed 8/24/11	Wed 8/24/11	151,152,153,154	Phoenix Building Inspector
156	*FINAL PLUMBING INSPECTION*	1 day	Wed 8/24/11	Wed 8/24/11	151,152,153,154	Phoenix Building Inspector
157	*FINAL ELECTRICAL INSPECTION*	1 day	Wed 8/24/11	Wed 8/24/11	151,152,153,154	Phoenix Building Inspector
158	*FINAL STRUCTURAL INSPECTION*	1 day	Wed 8/24/11	Wed 8/24/11	151,152,153,154	Phoenix Building Inspector
159	*FINAL HEALTH INSPECTION*	1 day	Thu 8/25/11	Thu 8/25/11	13,154,155,156,157,158	Health Department
